Previous references

Edn 69 of 97 1898-99 (Education)

Later references

File No 57

Serial Nos 1-2

GENERAL AND REVENUE SECRETARIAT

Serial Nos 1 — 2

~~Part~~ B for June 1899

SUBJECT

Village School Building at Kuderu Chamarajnagar Tq

Counterfoil Cheque Indexed

T Raghavachar

G R S 58

(19) Ed 237.

189

I have the honor to be,
Sir,
Your most obedient servant,

Insp Gen of Education

(81) 2

Ldn 06]

OFFICE OF INSPECTOR GENERAL OF EDUCATION IN MYSORE

No 6091/202 with 2 enclosures Mysore, ~~Bangalore,~~ 30th January 1899

From

H J BHABHA Esq,

Inspector General of Education in Mysore

To

The Secretary to the Government of Mysore,
General and Revenue Departments

Edn 694 97 Sec 2

+ ~~PR 681 V~~ Sec 5/97

With reference to Government Order No 13608-12 Ed Dt 20-96 of the 22nd April 1898 sanctioning the construction of a building of the III Village School design for the accommodation of the Hobli School at Kudera in the Chamrajnagar Taluk, I have the honour to inform you that the work of the new construction could not be put in hand till now for the reasons stated in my letter No 6090/201 and 6092/203 of this date. I request that Government may be pleased to sanction the construction of a building of the III Village School design for the accommodation of the Hobli School at Kudera Chamrajnagar Taluk, the cost being met

from the allotment provided for Buildings
in the Village School Fund Budget
of the current official year. The proposed
plan and estimate are forwarded
herewith for reference

I have the honour to be,
Sir,
your most obedient servant,

Hy Birch
Inspector General.

Encl to SF 1

DESIGN OF A VILLAGE SCHOOL No. 3

Scale 5′=1′

ESTIMATED COST Rs. 1,305

Average daily attendance not exceeding 100

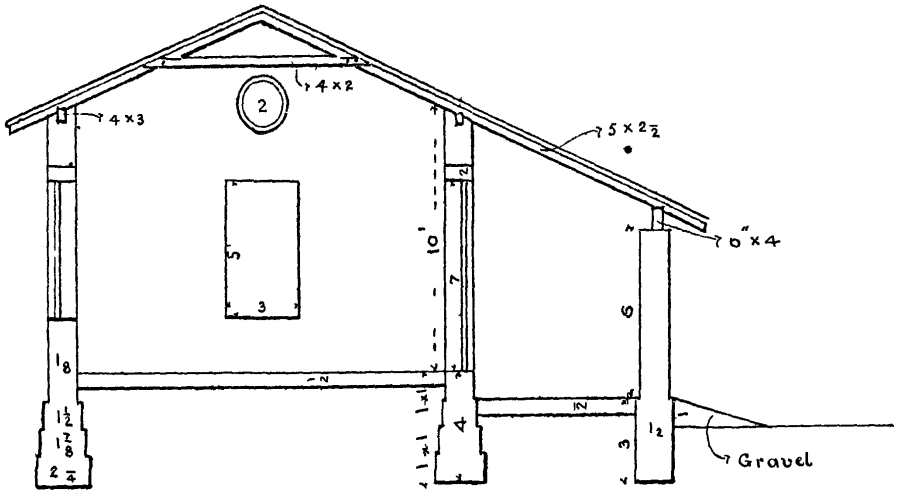

SECTION ON AB



Sri Rama Litho Press

PLAN

Mysore

5

ESTIMATE FOR CONSTRUCTING A HOBLI SCHOOL HOUSE

DESIGN No III

DETAILS OF WORK	No	DIMENSIONS L	B	D	CONTENTS	
MAIN BUILDING						
Earthwork Excavation —						
Front and rear walls	2	49	2	1	94	
End walls	3	13	2	1	94	
Total					318	Cyds 12
Brick Masonry —						
Foundation Front and rear walls	2	49	2	1	24	
End walls	3	13	2	1	94	
Basement Front and rear walls	2	49	1	1	186	
Do do	3	49	1	1	147	
End walls	3	14	1	1	80	
Do	3	13	1	1	62	
First and rear wall	2	48	1	1	146	
End wall	3	14	1	1	66	
Superstructure Footings walls	2	48	1	9_4	1 061	
End walls		15	1	10	506	
Gables over end walls	3	16	1_8	2	154	
Total					2 726	
Deductions —						
Doors	3	4	1	7	114	
Windows	8	3	1	5	173	
Circular Ventilat	2	5	1		11	
Lintel slab over door	3	7	1		12	
Do over windows	8	6	1		27	
Total deductions					337	
Balance Cft burnt Brick in chunam						Cft 2 389
Slabs stone & tile work—						
Lintel slab over door	3	7	1^1		24	
Do windows	8	6	1		54	
Slab at side of windows	8 × 2	2	2	(¾)	24	
Over step	2	5	1		10	
Total					11	Sft 112
White washing—						
Interior of Hall	1	90		10	900	
Do side room	1	60		10	600	
Exterior do	1	131		9	1 247	
Basement side and rear	1	83		2	166	
Do front	1	48		1	48	
Total						Sq 29 61

DETAILS OF WORK	No	Dimension L	B	D	Contents	
Teak wood work—						
Rafters $2\frac{1}{2}$ apart to Main building	20×2	11	$2\frac{1}{2}'$	5"	38 19	
Collars	20	10	2	4	11 11	
Wall plates	2	48	4	3	8 00	
Total						57 30
Teak wood Eave boards (8 ×1)	1	$48\frac{1}{2}$				Rft $48\frac{1}{2}$
Arch work in front of window to act as sunshade	8	$5\frac{1}{2}$	$\frac{3}{4}$	$\frac{3}{4}$		Cft 24
Gravel—						
To flooring Hall	1			$\frac{1}{3}$	8	
Do Room	1			$\frac{1}{3}$	4	
Total						Cyd 12
Teak wood doors (4 ×7)	3					No 3
Do windows (3 ×5)	8					No 8
Circular ventilator (2 D)	2					No 2
Mangalore tiled roof	2	$48\frac{1}{2}$	11			Sq 10 67
VERANDAH						
Earth work Excavation—						
Pillars	6	$1\frac{1}{2}$	$1\frac{1}{2}$	2	27	Cyd 1
Burnt Brick in chunam—						
Pillars	6	$1\frac{1}{2}$	$1\frac{1}{2}$	2	27	
Basement Pillars	6	$1\frac{1}{2}$	$1\frac{1}{2}$	1	14	
Superstructure do	6	1^1	$1\frac{1}{2}$	$\frac{5}{6}$	45	
Total						Cft 86
White washing—						
Pillars	6	$4\frac{1}{2}$		6	162	Sq 1 62
Teak wood—						
Rafters $2\frac{1}{2}'$ apart	20	$8\frac{1}{2}$	$2\frac{1}{2}$	5	14 ,5	
Summers	1	$48\frac{1}{2}$	4	6	8 08	
Total						Cft 22 83
Gravel—						
Flooring	1	$\frac{48'}{3}$		'	7	
Front	1		"	$\frac{0+1}{2\times3}$	4	
Total					11	Cyd, 11
Roofing with Mangalore tiles	1	$48\frac{1}{2}$	11		534	5 34

Abstract

DETAILS	UNIT	RATE			MAIN BUILDING		VERANDAH		TOTAL COST
		R	A	P	Q	C	Q	C	
Earth w k Exca t o	Cyd	0	2	0	12	2	1		2
Burnt br k n chunam fill ng f u d t n B S	Cft	0	2	9	2389	411	86	15	426
Do d l w k	Cft	0	4	0	24	6			
Ston slabs 6 th k	Sft	0	3	6	11[illegible]	25			2
Wl t wash g two coat	Sq	0	3	0	29 61	6	1 6[illegible]		6
Teak wo d wo k	Cft	3	8	0	57 30	201	22 83	80	281
Teak wo d Ea b a d (8 ×1)	Rft	0	4	0	48	12			12
Grav l	Cyd	0	8	0	12	6	11	6	12
Te k wood doo s	No	16	0	0	3	48			48
Do W ndows	N	16	0	0	8	1 8			128
C cula v nt l t	N	6	0	0	2	12			12
M ngalo e t les of g nclud ng ı dge t les	S1	18	0	0	10 67	192	5 34	96	288
Total						1 049		197	1 246
C nt g n s at 5 p r ce t						50		9	59
Grand Total Rupees						1 099		206	1 305

C T DALAL

Executive Engineer
Tumkur Division

Estimate for Constructing a Hobli School House,

DESIGN No III

Amount of Estimate Rs 1,305

8

Read ———

Letter No 6091/202, d 30th — January 1899, from the I Gl of Education, in Mys reporting that the work of constructing a new ~~school~~ building for the accommodation of the Hobli School at Kuderu, in the Chamrajnagar Taluk, which was sanctioned by Govt in ~~Govt~~ their Proceedings order No 13608-1 Ed F 20- dated 22nd april 1898 was not put in hand in that year as the plans and estimates of the village school building in general, had to be revised and requesting sanction for the construction of a building of the III Village School Design for the same school from the allotment for Buildings in the current years village — school Fund Budget, at Rs 1305 as per

Education
SCHEME
FILE No 52798
2
SI

* W.P. 5797/69 II

Edn 6 97

(82)

Enclosed
Rer plan and estimate
prepared by Mr C/T Dalal,
which excludes the D B W
establishment charges which
will have to be added to it
if the work is entrusted to
the agency of the D B W

Order thereon
No 14529-30 Ed-F-20-96
Dated 24th June 1896

Sanctioned
(2) The cost of Rs 1305 will
be met from the allotment
of Rs 10,000 for buildings
in the current year's village
school Fund Budget the estimate
may be raised by 10 % if the work
is to be carried out by the D B W

24/6/96

for Secretary

RCS

The Dfl. of Education, in Mysore
Comptroller, Mysore Government, with a copy
of the Abstract of the estimat
